

Highway 91/17 & Deltaport Way Upgrade Project

MONTHLY STATUS REPORT

Reporting Period: October 2019

1. PROJECT DASHBOARD

Project Delivery Objectives		Overall Project	DB Contractor	Owners/Other Works	Comments
Safety	Take every reasonable step to ensure that the work is performed safely and in compliance with all applicable safety regulations, and in accordance with government policy.	●	●	●	Safety meetings and orientations ongoing.
Budget	Delivered within the approved budget.	●	●	●	The Project has an approved capital budget of \$245 million and continues to track on budget.
Schedule	Delivered within the approved schedule.	●	●	●	All key Project activities are proceeding on schedule.
Scope	Deliver the approved scope.	●	●	●	Delivery of the specified components is on track.
Indigenous Groups	Continue to build and maintain a positive collaborative working relationship	●	●	●	Discussions and consultation with Indigenous groups ongoing.
Environmental	Ensure the work is performed in an environmentally responsible manner.	●	●	●	The Project will be delivered in accordance with the obligations identified in the Overview Environmental Effects Assessment.
Community Benefits	Incorporate the Community Benefits Objectives into the Project.	●	●	●	Community Benefits Objectives outlined in the Design-Build Agreement for implementation by the Design-Build Contractor.
Third Parties	Continue to build and maintain positive relationships with Project Partners and other third parties.	●	●	●	Early and frequent engagement and advancing agreements with Project partners and other third parties.
Stakeholder Engagement	Continue to build and maintain positive relationships with the community, and other stakeholders.	●	●	●	Engagement with key Project partners is ongoing. Community and stakeholder engagement will continue.
Quality	Implement an effective Quality Management System.	●	●	●	Quality audits and reviews performed as required per the Quality Management Plan.


Status	Description
●	Not currently applicable, as the Project is in Procurement Phase
●	Managing some issues, negotiating resolution; required immediately
●	Managing some issues, negotiating resolution; required in the near term
●	Good progress

2. Introduction

Project Overview

The Highway 91/17 and Deltaport Way Upgrade Project is a combination of improvements to the existing Highway 91, Highway 17, Highway 91 Connector and Deltaport Way to improve travel safety, reliability and efficiency. These upgrades will improve local and commercial travel time and reliability in the area, reduce conflicts between commercial vehicles and other traffic, and support community and economic development. The Highway 91/17 components also complement the recently completed 72nd Avenue Interchange Project and the Alex Fraser Bridge Project currently underway.

The Project is being funded by the Province of British Columbia, the National Infrastructure Component of the New Building Canada Fund, the Vancouver Fraser Port Authority and the Tsawwassen First Nation, and is being delivered by the Ministry.

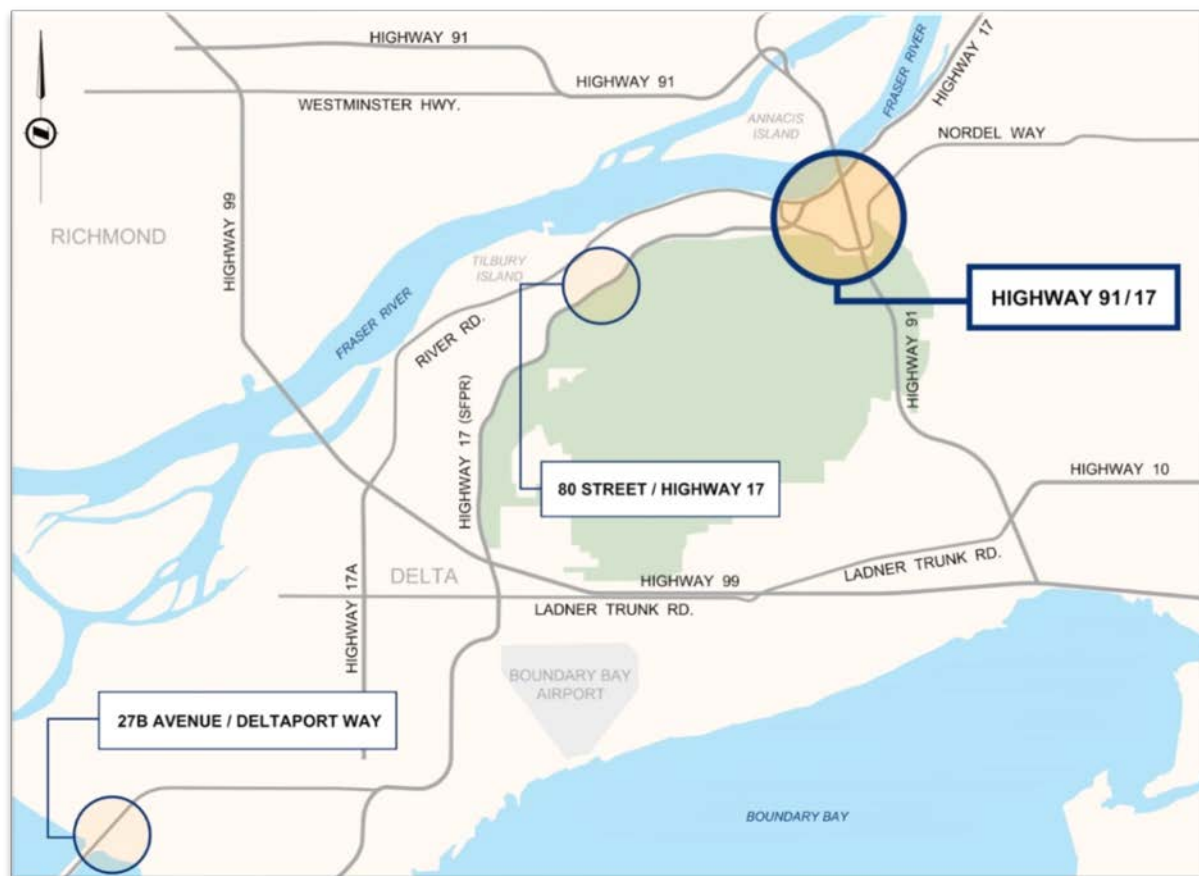

Project Goals

The Project will:

- Improve travel time and reliability through Delta, with congestion-reduction travel time savings
- Improve traffic safety for goods movers and the travelling public, with lowered collision risk and better operating hours at the Nordel commercial vehicle inspection facility
- Support community and economic development, with better access to employment areas, faster access between South Delta and North Delta/Surrey, improved access to cycling connections, and improved permitting and inspection service for commercial vehicle operators

Key Milestones Achieved to Date

Key milestones achieved to date are listed by category below. The available corresponding reports can be found within the Document Library of Highway 91/17 and Deltaport Way Upgrade Project website at www.gov.bc.ca/highway91-17-deltaport.

Engagement	<ul style="list-style-type: none">• Conducted Public Information Open House• Released Engagement Summary Report (2018)
Third Parties	<ul style="list-style-type: none">• Draft Municipal Agreement with City of Delta• Metro Vancouver Board has approved the Accommodation Agreement; Parties working to final documentations
Environmental Review	<ul style="list-style-type: none">• Reviewed relevant South Fraser Perimeter Road (SFPR) studies and conducted additional baseline studies• Developed Overview Environmental Effects Assessment (OEEA) Terms of Reference• Finalized OEEA based on input from Indigenous Groups and stakeholders• Acceptance from Environmental Assessment Office (EAO) that amendment to SFPR EAC is not required
Agriculture	<ul style="list-style-type: none">• Submitted Agricultural Land Commission (ALC) application• Approval with conditions received from ALC (2018)
Indigenous Groups	<ul style="list-style-type: none">• Capacity agreements for the OEEA (2018)
Design/Engineering	<ul style="list-style-type: none">• Prepared reference design concept• Completed traffic data and analysis• Completed geotechnical investigations and reports
Design-Build Agreement	<ul style="list-style-type: none">• Issued Request for Qualifications (RFQ) for Highway 91/17 upgrades• Issued Request for Proposals (RFP) for Highway 91/17 upgrades• Issued Definitive Design-Build Agreement• Received and evaluated Technical Submittals• Issued invitations to submit Financial Submittals• Received and evaluated Financial Submittals• Selected Preferred Proponent
Owner-Led Work	<ul style="list-style-type: none">• Awarded Deltaport Way Ramp Improvements construction contract• Awarded 27B Avenue Improvements construction contract• Awarded Deltaport Way to 27B paving construction contract• Completed work on Deltaport Way Ramp Improvements• Substantial completion achieved on 27B Avenue Improvement Project
Property Acquisition	<ul style="list-style-type: none">• Completed four of five property acquisitions

October 2019 Highlights


Project highlights this month include:

Engagement	<ul style="list-style-type: none">• Ongoing response to public and stakeholder enquiries• Communications to support 27B Avenue Project completion
Design/Engineering	<ul style="list-style-type: none">• Coordination with City of Delta on future drainage works• Project team preparing and calibrating a new drainage model
Environment	<ul style="list-style-type: none">• Final OEEA Posted to Data Room and Project website, and distributed to interested stakeholders• Engagement with Indigenous Groups undertaken regarding specialized archaeological analysis• AIA interim report #2 in progress. Site Alteration Permit to be resubmitted to Ministry of Forests, Lands, Natural Resource Operations and Rural Development (FLNRO) with comments incorporated from Indigenous Groups• Ongoing engagement with Ministry of Environment (MOE) in support of Abandonment Approval Application• Ground water and surface water monitoring report completed.
Design-Build Agreement	<ul style="list-style-type: none">• Preferred Proponent selected• Ongoing discussions and negotiations with Preferred Proponent
Owner-Led Work	<ul style="list-style-type: none">• Contract award and construction underway for additional paving between Deltaport Way and 27B Avenue.• Substantial completion achieved, landscaping ongoing on 27B Avenue Improvements Project

3. SCHEDULE

The following schedule depicts deliverables, milestones and associated dates and timelines for the planning and procurement phases of the Project, as well as anticipated construction timelines.

Schedule denotes calendar year.

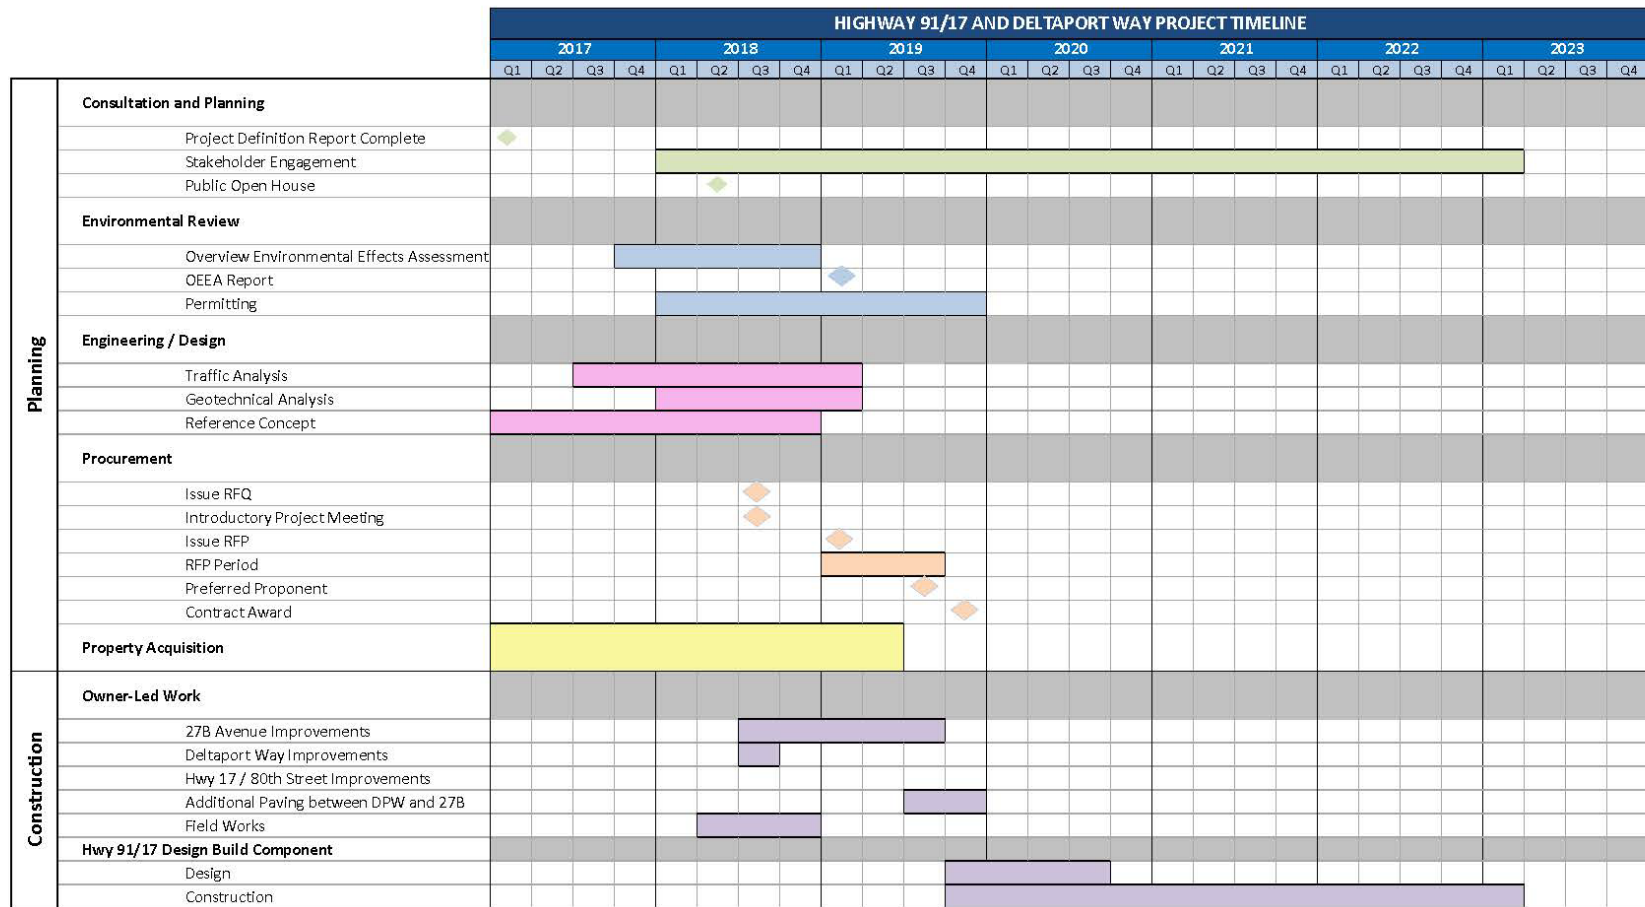

4. PROJECT DELIVERY

Safety

Objectives	<ul style="list-style-type: none">• Ensure a safe worksite at all times• Provide clear information on health and safety responsibilities• Ensure all required training is provided and evaluated• Ensure that Project activities are in accordance with the Workers Compensation Act and WorkSafeBC Health and Safety Regulations
Accomplished in October 2019	<ul style="list-style-type: none">• Conducted onsite safety orientations• Provided regular safety reminders for field staff
Key activities for Next 3 months	<ul style="list-style-type: none">• Provide ongoing safety training as required• Provide Project safety orientation as required

Quality

Objectives	<ul style="list-style-type: none">• Ensure design services and construction works delivered to the Province are implemented within a quality standard consistent with Ministry standards and ISO 9001• Ensure internal processes are conducted per Project quality requirements, consistent with Ministry standards and ISO 9001
Accomplished in October 2019	<ul style="list-style-type: none">• Ongoing review and revision of Project Quality Management Plan
Key activities for Next 3 months	<ul style="list-style-type: none">• Continue quality management input and support to procurement activities• Ongoing review of internal processes

Project Controls

Objectives	<ul style="list-style-type: none">• Effectively manage the Project's contracts, scope, schedule and cost• Implement an efficient document control and records management system• Ensure Project controls are governed by provincial policies such as the Ministry of Finance Capital Asset Management Framework and the Core Policy and Procedures Manual• Ongoing updates to Project Management Plan
Accomplished in October 2019	<ul style="list-style-type: none">• Held regular Project control meetings with discipline leads
Key activities for Next 3 months	<ul style="list-style-type: none">• Continue regular Project control meetings with discipline leads• Review Project risk register based upon award of Design-Build Contract• Monitor Project schedule, scope and budget

5. Project Development

Stakeholder Engagement

Scope	<ul style="list-style-type: none">• Manage ongoing public and stakeholder consultation, community relations and Project communications
Accomplished in October 2019	<ul style="list-style-type: none">• Ongoing enquiry response• Communications to support 27B Avenue Project completion
Key activities for Next 3 months	<ul style="list-style-type: none">• Continue community and stakeholder engagement• Ongoing enquiry response• Communications to support procurement milestones• Business and community group presentations upon request

Environment

Scope	<ul style="list-style-type: none">• Develop OEEA and supporting environmental reports• Manage Project monitoring and permitting process• Ensure the Project adheres to obligations defined within the SFPR Project Environmental Assessment Certificate (EAC) Table of Commitments and Assurances (TOCA)
Accomplished in October 2019	<ul style="list-style-type: none">• Ongoing engagement with MOE in support of Abandonment Approval Application• Final OEEA Posted to the Data Room and the project website.• Technical Memo regarding Summary and Recommendation for Analysis of samples reviewed by Indigenous Groups, follow-up meetings held or being arranged as requested• AIA interim report #2 in progress.• Site Alteration Permit revised and to be re-submitted to FLNRO including comments provided by Indigenous Groups, pending follow-up meetings• Ground water and surface water monitoring report completed and ready to be distributed to stakeholders.
Key activities for Next 3 months	<ul style="list-style-type: none">• Update Site Alteration Permit Application (Section 12) based on additional feedback received from FLNRO & Indigenous Groups and resubmit to FLNRO• Complete and submit AIA interim report #2• Section 14 Final Permit Report to be drafted• Update drainage model based on calibration data obtained• Continue work in support of Abandonment Approval application to MOE in relation to Sunbury Mounds• Obtain Water Sustainability Act (WSA) Permit for Delta Nature Reserve Boardwalk Project from FLNRO

Agriculture

Scope	<ul style="list-style-type: none">• Develop appropriate plans to mitigate potential agricultural effects of the Project
-------	---

Accomplished in October 2019	<ul style="list-style-type: none"> No Actions
Key activities for Next 3 months	<ul style="list-style-type: none"> Monitor compliance of approval conditions during construction

Indigenous Groups

Scope	<ul style="list-style-type: none"> Consultation and engagement with Identified Indigenous Groups
Accomplished in October 2019	<ul style="list-style-type: none"> Provided Project updates as required Focused consultation regarding archaeological finds in the Project area Incorporated comments from Indigenous Groups into the final OEEA and distributed to Indigenous Groups.
Key activities for Next 3 months	<ul style="list-style-type: none"> Continue engagement with Indigenous Groups, including meetings and site visits as requested Discuss Project related opportunities and benefits with Indigenous Groups

Design-Build Agreement

Scope	<ul style="list-style-type: none"> Develop a business case, RFQ, RFP and subsequent evaluation of submissions Development and award of tender packages for Design-Bid-Build Contracts
Accomplished in October 2019	<ul style="list-style-type: none"> Preferred Proponent selected and notified Ongoing discussions and negotiations with Preferred Proponent
Key activities for Next 3 months	<ul style="list-style-type: none"> Continue the Competitive Selection Process Conclude negotiations with Preferred Proponent Finalize and execute Design Build Agreement

Design/Engineering

Scope	<ul style="list-style-type: none"> Develop a design concept, technical requirements/specifications and related technical studies for the Project Conduct Project related traffic operations modelling, data collection, and other related engineering services Provide technical input to the procurement and environmental processes Conduct compliance reviews of work by the Design-Build Contractor
Accomplished in October 2019	<ul style="list-style-type: none"> Undertook additional traffic modelling analysis of the Project area Ongoing update and calibration of drainage model.
Key activities for Next 3 months	<ul style="list-style-type: none"> Provide technical support for procurement Update and calibration of drainage model based on results of baseline ground water and surface water monitoring program Engagement with Delta to provide data required for future drainage system

Owner-Led Works

Scope	<ul style="list-style-type: none">Overall planning, coordination and implementation of construction activities
Accomplished in October 2019	<ul style="list-style-type: none">Remaining 27B works ongoing including deficiency work, correction of non-conformances, and completion of landscaping works.Ongoing construction at DPW-27B Additional paving including civil and drainage works.
Key activities for Next 3 months	<ul style="list-style-type: none">Total completion of 27B Project and close out of any open claims. Complete DPW to 27B Paving Project.

Property Acquisition

Scope	<ul style="list-style-type: none">Acquire land rights to deliver the Project (majority of the Project falls within existing highway boundaries)
Accomplished in October 2019	<ul style="list-style-type: none">Continued discussions with owner re access arrangements (ongoing)
Key activities for Next 3 months	<ul style="list-style-type: none">Continue property discussions with remaining property owner to secure final agreement (ongoing)Continue discussion for Statutory Right of Way agreement with Vancouver Fraser Port AuthorityConduct legal surveys on all required properties to perfect tenure as road or highway (ongoing)

6. Project Cost Report

- To date, \$36 million has been spent on the Project
- The approved capital Project budget is \$245 million
