



Client :
Imperial Oil

Borehole No. : 13-50

Location :
1389 Main Street, Penticton, BC

(Page 1 of 3)

Drilling Contractor: D&L Septic Service/Mud Bay
Drilling Method : Hydrovac/Vibratory Sonic
Borehole Dia. (m) : 0.15
Pipe/Slotted Pipe Dia. (m): 0.05, 0.05

Date Monitored : 2013 08 13
Ground Surf Elev. (m) : 361.028
Top of Casing Elev. (m) : 360.959

Project Number : 132059
Borehole Logged By : IPC
Date Drilled : 2013 07 22
Log Typed By : SW

Depth in Metres	Drilling Legend	Water/FP Levels	Stratigraphy Plot	Sample Interval/ Core Run	Sample Number	Blow Count	% Recovery	Soil Vapour (% LEL)	Well Name: 13-50
	Sample Interval Water Level 1 Water Level 2 FP FP	Reading within indicated scale Reading outside indicated scale							
	Soil Description							0 20 40 60 80 100	Solid PVC Slotted PVC Road Box Concrete Silica Sand Bentonite
0	SILTY SAND (FILL), fine to medium grained, some subangular gravel, light grey, dry. - at 0.3 m - becomes fine to coarse grained, some fine to coarse subangular gravel, trace silt, trace cobbles, medium brown, moist, rootlets, some plastic garbage, styrofoam - at 0.9 m - becomes some cobbles, no more garbage								
1									
2	SAND, fine to coarse grained, some silt, some fine to coarse subangular gravel, some subrounded cobbles, medium brown, damp. - between 2.4 m and 3.1 m - becomes light grey								
3									
4									
5	- at 4.6 m - becomes cobbly, some boulders								
6									
7	- at 6.1 m - becomes medium brown, moist - between 6.1 m and 13.1 m - drill casing broke - 150 mm steel casing left in ground								
8	- between 7.6 m and 8.2 m - becomes some medium grey clouring								
9									
10	GRAVELLY SAND, wet (from drilling)								
...Continued <p>Notes: Boded sample denotes sample analyzed.</p>									

Print Date: 2014 06 25, Date Approved: 2014 06 25



Client :
Imperial Oil

Borehole No. : 13-50


Location :
1389 Main Street, Penticton, BC

(Page 2 of 3)

Drilling Contractor: D&L Septic Service/Mud Bay
Drilling Method : Hydrovac/Vibratory Sonic
Borehole Dia. (m) : 0.15
Pipe/Slotted Pipe Dia. (m): 0.05, 0.05

Date Monitored : 2013 08 13
Ground Surf Elev. (m) : 361.028
Top of Casing Elev. (m) : 360.959

Project Number : 132059
Borehole Logged By : IPC
Date Drilled : 2013 07 22
Log Typed By : SW

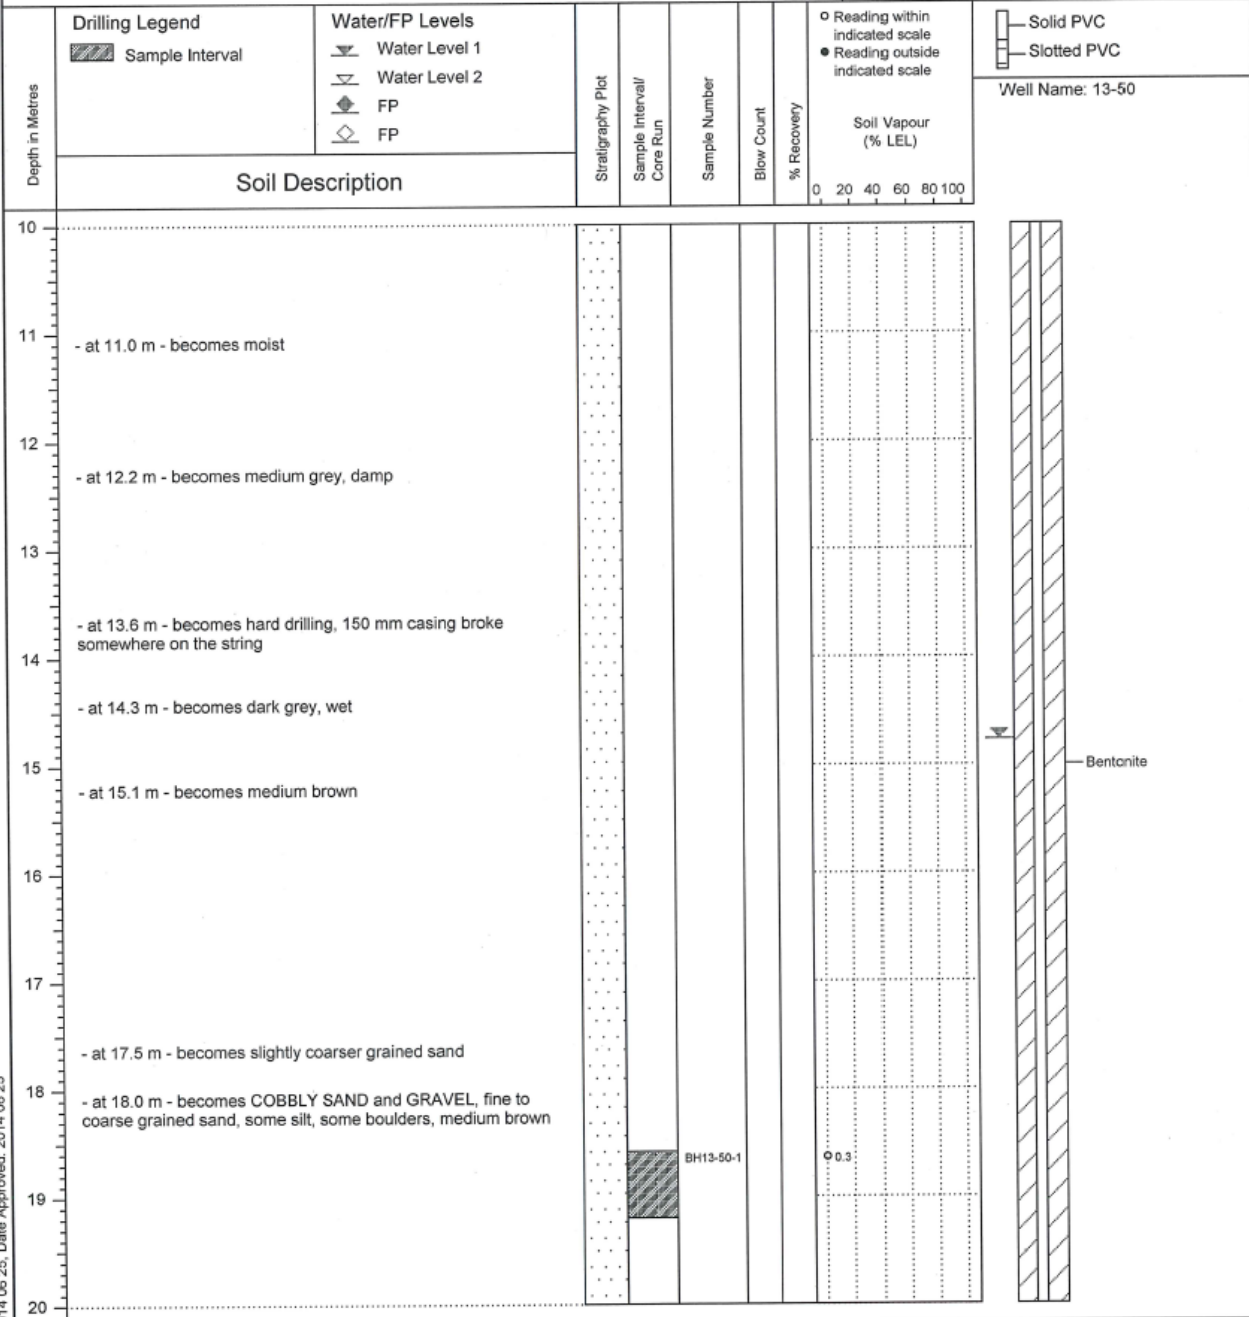

Print Date: 2014 06 25, Date Approved: 2014 06 25

...Continued

Notes:
Bolded sample denotes sample analyzed.



Client :
Imperial Oil

Borehole No. : 13-50


Location :
1389 Main Street, Penticton, BC

(Page 3 of 3)

Drilling Contractor: D&L Septic Service/Mud Bay
Drilling Method : Hydrovac/Vibratory Sonic
Borehole Dia. (m) : 0.15
Pipe/Slotted Pipe Dia. (m): 0.05, 0.05

Date Monitored : 2013 08 13
Ground Surf Elev. (m) : 361.028
Top of Casing Elev. (m) : 360.959

Project Number : 132059
Borehole Logged By : IPC
Date Drilled : 2013 07 22
Log Typed By : SW

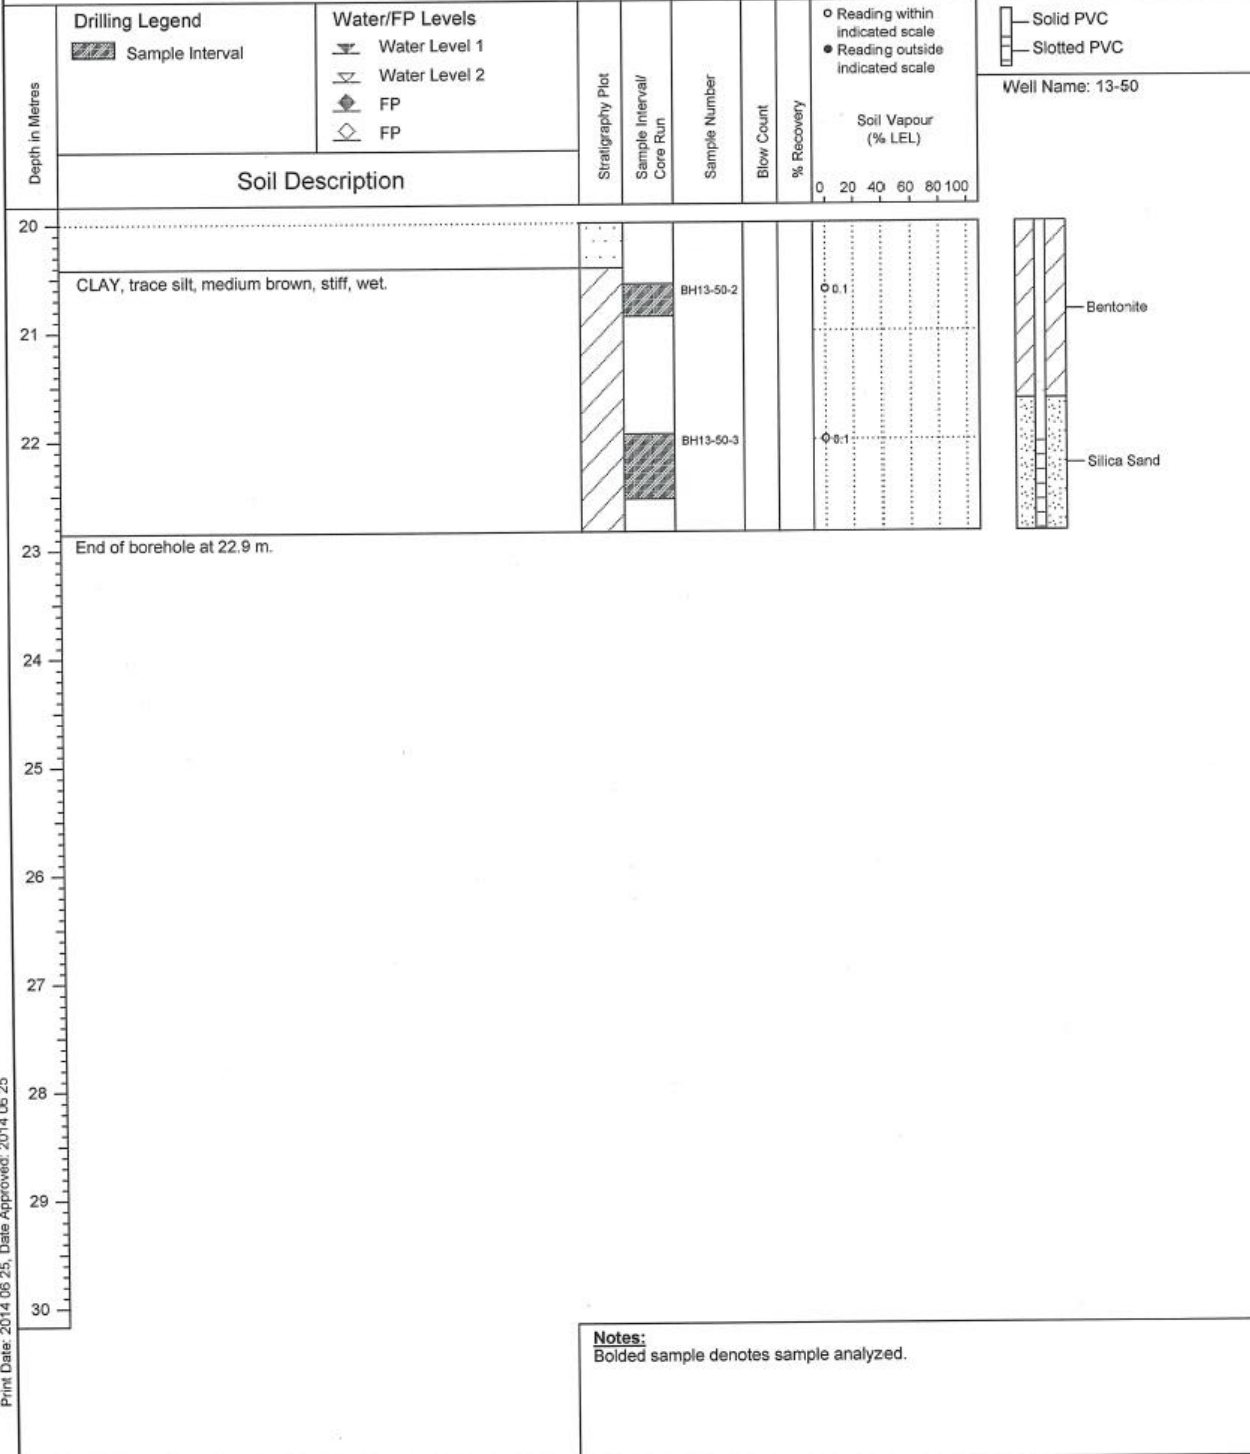

Notes:
Bodied sample denotes sample analyzed.

Print Date: 2014 06 25, Date Approved: 2014 06 25
